

**DUY TAN UNIVERSITY
INTERNATIONAL SCHOOL**



GROUP PROJECT

**PROJECT E-BANKING PHISHING WEBSITE
DETECTION SYSTEM**

CLASS: CMU-IS 432 CIS

GROUP 3

Instructor : Mr Nguyen Duc Man

Team Members: Nguyen Van Duy Manh

Le Minh Truong Kha

Nguyen Xuan Loc

Dang Dai Viet

Tran Viet Loc

Da Nang, November 4, 2025

PROJECT INFORMATION

Project Title	PROJECT E-BANKING PHISHING WEBSITE DETECTION SYSTEM		
Start Date	October 1,2025	End Date	December 15, 2025
Lead Institution	International School, Duy Tan University		
Project Mentor	Mr Nguyen Duc Man		
Product Owner & Contact Details	Dang Dai Viet Email: vdang9721@gmail.com ID: 29211155820		
Members	Nguyen Van Duy Manh	duymanhhdvn1@gmail.com	29211100024
	Le Minh Truong Kha	khatruong2k5@gmail.com	29211158908
	Nguyen Xuan Loc	xuanlocmtp@gmail.com	29211158251
	Dang Dai Viet	vdang9721@gmail.com	29211155820
	Tran Viet Loc	tranvietloc288@gmail.com	29211352994

DOCUMENT HISTORY

Version	Person	Date	Description
1.0	Full Team	October 1, 2025	Project Charter
1.1	Full Team	November 4-11, 2025	Requirement list (prioritized) Work Breakdown Structure (WBS) Activity list with estimates PERT/CPM
1.2	Full Team	November 13-30, 2025	Sprint Backlog Product Backlog Burndown Chart Budget Demo Interface Gantt Chart

SIGNATURE

Document Approvals: *The following signatures are required for approval of this document.*

Mr Nguyen Duc Man		Date:
Nguyen Van Duy Manh		Date:
Le Minh Truong Kha		Date:
Nguyen Xuan Loc		Date:
Dang Dai Viet		Date:
Tran Viet Loc		Date:

CONTENTS

I. Project Charter	4
1. Background.....	4
2. Project Goal	4
3. Project Team	5
4. Benefits, Costs and Budget.....	5
5. Scope and Exclusion.....	6
6. Deliverables	6
7. Measuring Success.....	6
II. Requirement List	7
1. EPIC A - Accounts & Authentication :	7
1.1. US-A1 Register :	7
1.2. US-A2 Login / Logout :	7
1.3. US-A3 Change Password / Forgot Password :.....	8
2. EPIC B - Website Checking (Core User Functionality) :.....	8
2.1 US-B1 Check Website (URL Scan) :	8
2.2. US-B2 View Detailed Analysis :	8
2.3. US-B3 Save / View Scan History :.....	8
3. EPIC C - Blacklist Management (Admin) :.....	9
3.1. US-C1 Add to Blacklist (Admin) :.....	9
3.2. US-C2 Remove/Update Blacklist Entry (Admin).....	9
3.3. US-C3 Bulk Import / Export Blacklist :.....	9
4. EPIC D - Classification Model & Data Pipeline :	9
4.1. US-D1 Integrate Classification Model :.....	9
4.2. US-D2 Model Accuracy Monitoring :.....	10
4.3. US-D3 Retrain Pipeline & Update DB :	10
5. EPIC E - Feedback & Reporting :	10
5.1. US-E1 User Feedback on Results :	10
5.2. US-E2 Admin Review Queue :	10
6. EPIC F - Database & Data Requirements :	11

6.1. US-F1 Blacklist database building (≥ 500 verified websites) :	11
6.2. US-F2 Efficient Query Performance :	11
7. EPIC G - UI/UX & Notifications :	11
7.1. US-G1 Friendly Home Page and Help :	11
7.2. US-G2 Notifications for Admin Actions :	11
8. EPIC H - Non-Functional & Compliance :	11
8.1. US-H1 Security & Privacy :	11
8.2. US-H2 Performance & Scalability :	12
III. Work Breakdown Structure(WBS).....	13
IV. Activity List With Estimates	14
V. PERT/CPM	15
1. Project Activity List and Immediate Predecessors	15
2. PERT DIAGRAM.....	16
3. CPM Analysis	17
VI. Gantt Chart.....	18
VII. Risk Analysis	18
VIII. Budget.....	20
1. Human Resources	20
2. Reusable Resources	23
3. Consumed Resources.....	23
4. Total Project Budget Summary.....	24
5. Financial Feasibility & ROI.....	25
IX. Product Backlog.....	26
X. Burndown Chart	28
1. Sprint 1.....	28
2. Sprint 2.....	30
3. Sprint 3.....	31
4. Sprint 4.....	33
5. Sprint 5.....	34
6. Spint 6.....	35

XI. Sprint Backlog.....	37
1. Sprint 1	37
2. Sprint 2.....	38
3. Sprint 3.....	39
4. Sprint 4.....	40
5. Sprint 5.....	40
6. Sprint 6.....	41
XII. Use Tool Click Up	42
XIII. Demo Interface	45
XIV. Contribute Work	47

I. Project Charter

1. Background

Business Case / Background

Why are we doing this?

- The number of e-banking phishing websites is increasing, directly threatening users' finances and personal information.
- Users lack simple and effective tools to check the safety of banking websites before making transactions.
- E-commerce enterprises need a reliable solution to protect their customers during the payment process.
- **Ex:** Phishing attacks against financial institutions accounted for about 23% in Q2 2023, while payment services were hit by about 6% phishing attacks in 2024
- **Detailed Source:** <https://keepnetlabs.com/blog/top-phishing-statistics-and-trends-you-must-know>

2. Project Goal

Project Goal

SMART: *Specific, Measurable, Attainable, Relevant, and Time-bound*

- Successfully deployed web application with described functions and database within 4 months of project implementation.
- Build a database containing at least 500 verified and continuously updated phishing websites.
- Achieve > 99% accuracy when testing with phishing websites.
- Complete all documentation including reports, user guides and source code before the end of the course.

3. Project Team

Project Team

Project Sponsor: Nguyen Duc Man

Product Owner: Dang Dai Viet

Scrum Master: Nguyen Van Duy Manh

Development Team: Nguyen Van Duy Manh (Scrum Master), Le Minh Truong Kha, Nguyen Xuan Loc, Tran Viet Loc, Dang Dai Viet (PO, Support).

Additional Stakeholders: End-users, e-commerce businesses.

4. Benefits, Costs and Budget

Benefits, Costs, and Budget

Benefits:

- For Users: Safer online transactions, avoiding the risk of being scammed by fake websites.
- For Businesses: Increase customer trust in the brand.
- For Development Team: Accumulate experience and skills for similar jobs in the future.

Costs:

- Opportunity Cost: Time for research and development by members.
- Incidental Costs (if any): Domain, hosting, computational resources (if deploying complex models).

Budget needed:

- 800,000,000 VND - 900,000,000 VND (needed to purchase proprietary software, support services or specialized databases. Expenses for workspace, meals, equipment and salaries support team members).

5. Scope and Exclusion

Scope and Exclusion

In-Scope:

- Develop a web application with 6 functional modules as described.
- Integrate a classification algorithm based on URL, Domain Identity, Security, and Encryption features.
- Build a user-friendly, easy-to-use interface.

Out-of-Scope:

- Separate mobile applications (iOS/Android).
- The system cannot block access or automatically report phishing websites to authorities.
- Does not guarantee 100% accuracy for all newly emerging phishing websites.

6. Deliverables

Deliverables

1. Complete Web Application: User and admin interfaces with all 6 described functionalities.
2. Classification Model: Integrated data mining algorithm for automatically evaluating suspicious URLs.
3. Project Documentation: Technical report, installation/user guide, presentation slides, and source code.

7. Measuring Success

Measuring Success

What is acceptable:

1. The web application runs smoothly for users to register, log in and check URL within 5 seconds.
2. The classification algorithm achieves at least 90% accuracy when evaluated on the provided test dataset.

3. The blacklist management system is efficient, allowing administrators to easily add/remove and update items.
4. All documentation and source code are submitted on time..

II. Requirement List

1. EPIC A - Accounts & Authentication :

1.1. US-A1 Register :

- As a visitor, I would like to register an account (email + password + optional profile information) so I can use the system to check out sites and save my history.
- Acceptance Criteria:
 - User can create account with valid email and password.
 - Confirmation email sent (or success page) and account activated.
 - Error shown for duplicate email or invalid input.

1.2. US-A2 Login / Logout :

- As a registered user, I want to log in and out securely so that my personal information and history remain private.
- Acceptance Criteria:
 - Valid credentials allow login; invalid show error.
 - Session established and terminates on logout.
 - Login page rate-limits repeated failures.
- As an Admin, I want to log in and log out using an administrator account, so that I can securely access administrative features (e.g., blacklist management, feedback review, system monitoring).
- Acceptance Criteria:
 - Admin must log in using a separate admin login page or a role-based access level different from regular users.
 - Admin can access the Admin Dashboard only after successful authentication.
 - If login credentials are invalid, an error message is displayed.
 - After logging out, the admin cannot access any admin pages and is redirected to the admin login page.
 - Admin session expires automatically after a security timeout.

1.3. US-A3 Change Password / Forgot Password :

- As a registered user, I want to change my password and reset via email if forgotten so that I can regain access securely.
- Acceptance Criteria:
 - Users can change their password once authenticated.
 - "Forgot Password" will send a password reset link that is valid for a limited time.
 - The new password must meet the complexity rules (capital letters, numbers, special characters).

2. EPIC B - Website Checking (Core User Functionality) :

2.1 US-B1 Check Website (URL Scan) :

- As a user, I want to type in a URL and get instant results (safe/suspicious/scam) to know whether to trust that site or not.
- Acceptance Criteria :
 - The system returns results within the target latency range (ex : <5 seconds).
 - The results include a brief explanation (blacklist error, suspicious feature, trust).
 - If the URL is not properly formatted, the user will see a helpful error.

2.2. US-B2 View Detailed Analysis :

- As a user, I would like to see detailed analytics (features used by the classifier: domain age, SSL, domain identity, keywords, etc.) to understand why the site was flagged.
- Acceptance Criteria :
 - Detailed reports show features used and classifier confidence scores.
 - Links to recommended resources or actions (no login required).
 - Human-readable reports stored in session/history.

2.3. US-B3 Save / View Scan History :

- As a logged in user, I would like to save recent scans to my account so I can review previous checks.
- Acceptance Criteria :
 - Scan history lists URL, date/time, result, and link to detail.
 - User can delete individual history items.

- History accessible only to the user.

3. EPIC C - Blacklist Management (Admin) :

3.1. US-C1 Add to Blacklist (Admin) :

- As an admin, I want to add users that are considered untrustworthy or dangerous to a blacklist so that the system immediately blocks or flags them.
- Acceptance Criteria :
 - Admin interface to add URL/domain with reason and source.
 - New blacklist entries take effect immediately during audits.
 - Audit trail records admin info, timestamp, reason.

3.2. US-C2 Remove/Update Blacklist Entry (Admin)

- As an admin, I want to edit or delete blacklist entries so that I can correct false positives.
- Acceptance Criteria :
 - Administrators can search, edit reason/metadata, or delete entries.
 - The system records edits/deletions for tracking.
 - Deletions will trigger a re-evaluation of previously flagged audits (if wanted).

3.3. US-C3 Bulk Import / Export Blacklist :

- As an admin, I want to import/export blacklist data (CSV/MySQL) so we can maintain a large verified database.
- Acceptance Criteria :
 - Admins can upload CSV files with validation and preview.
 - Import will show summary (added/failed).
 - Export will provide snapshot of current blacklist.

4. EPIC D - Classification Model & Data Pipeline :

4.1. US-D1 Integrate Classification Model :

- As a system, I want a classification model that evaluates URLs using URL features, domain recognition, security, and encryption so that the system can automatically detect suspicious websites.
- Acceptance Criteria :
 - The model endpoint can be called by the application/backend.
 - The model returns label + confidence.

- Integration tests show that the model is accessible and the results are parsed correctly.

4.2. US-D2 Model Accuracy Monitoring :

- As a PO/engineering lead, I want to have reporting on model accuracy on validation/test sets and metrics so we can maintain our target of >90% accuracy.
- Acceptance Criteria :
 - Periodic evaluations generate a precision/error matrix.
 - Alerts are triggered if the precision falls below a threshold.
 - Model version management and rollback

4.3. US-D3 Retrain Pipeline & Update DB :

- As a data engineer, I want to have a pipeline to retrain the model with updated labeled data so that the system can improve its detection ability over time.
- Acceptance Criteria :
 - The retraining process will take in new verified fraud records.
 - The new model is deployed after passing the test.
 - The retraining log and dataset snapshot are saved.

5. EPIC E - Feedback & Reporting :

5.1. US-E1 User Feedback on Results :

- As a user, I want to give feedback (“is this a scam” / “is this safe”) on the scan results so the system can get human input to improve the blacklist/model.
- Acceptance Criteria :
 - The feedback form is available on the results page.
 - Feedback is stored with the user ID (if logged in) and timestamp.
 - Aggregated feedback can be viewed by the admin/ML team.

5.2. US-E2 Admin Review Queue :

- As an admin, I would like to have a queue of user reported URLs to review so I can validate and update blacklist or model labels.
- Acceptance Criteria :
 - The queue lists items, user feedback, and previous triage results.
 - Admins can mark as verified scam, false positive, or need more information.
 - Actions are logged.

6. EPIC F - Database & Data Requirements :

6.1. US-F1 Blacklist database building (≥ 500 verified websites) :

- As a project, we wanted to have a MySQL database containing ≥ 500 verified and continuously updated phishing sites so that the model and tests use rich and up-to-date data.
- Acceptance Criteria :
 - Database schema includes tables for users, blacklists, scans, feedback, promotions, logs.
 - Initial import of ≥ 500 verified fraud profiles.
 - Administrative user interface to view/update profiles.

6.2. US-F2 Efficient Query Performance :

- As a system, I want DB queries to check URLs to respond within a target time (ex : ≤ 5 seconds) so that the user has a fast experience.
- Acceptance Criteria :
 - Indexes added on frequently queried fields.
 - Load testing shows acceptable latency under expected load.

7. EPIC G - UI/UX & Notifications :

7.1. US-G1 Friendly Home Page and Help :

- As a new user, I want clear instructions and explanations of the tool's functionality so I can trust and know how to use it.
- Acceptance Criteria :
 - Home page explains purpose, limitations and quick checkboxes.
 - Links to user guide and contact/report form.

7.2. US-G2 Notifications for Admin Actions :

- As an admin, I want to be notified when important events occur (ex : model drop, large report volume) so I can respond quickly.
- Acceptance Criteria :
 - Configurable alerts sent via email or dashboard.
 - Critical thresholds are defined and tested.

8. EPIC H - Non-Functional & Compliance :

8.1. US-H1 Security & Privacy :


- As a system owner, I want user credentials and sensitive data stored securely (hashed passwords, HTTPS) so user data is protected.

- Acceptance Criteria :
 - Passwords are hashed using a secure algorithm.
 - All pages are served over HTTPS.
 - Basic OWASP protections (input validation, rate limiting).

8.2. US-H2 Performance & Scalability :

- As a product owner, I want the web application to be able to handle the expected amount of concurrent users without taking more than 5 seconds to respond so that users can check the site quickly.
- Acceptance Criteria :
 - Load test report with acceptable metrics.
 - Caching is deployed for regular testing.

III. Work Breakdown Structure(WBS)

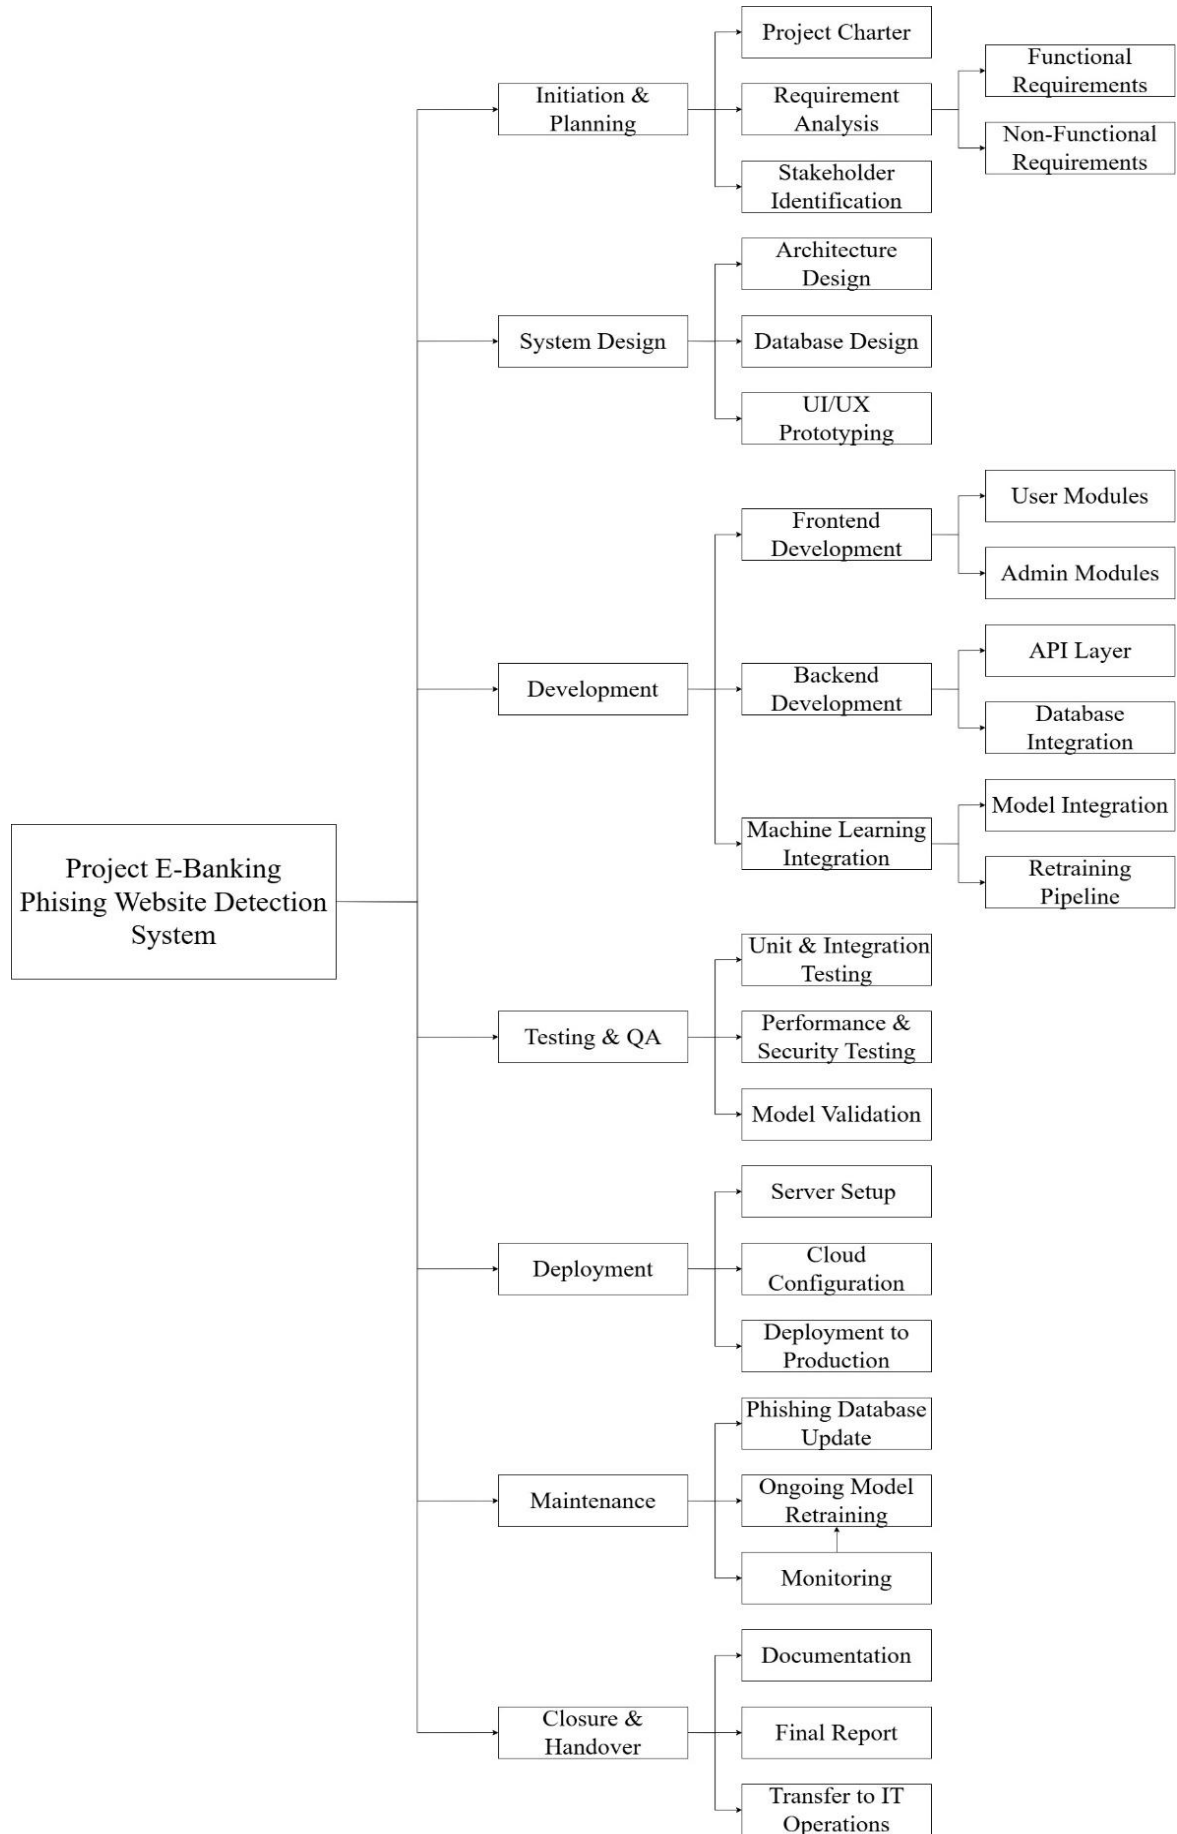

IV. Activity List With Estimates

- 1 Point = 1 Day
- 1 person works 1 day for 8 hours

ID	Activity	Story Point (Fibonacci)	Resource (persons)	Effort (hours)
PB01	Project Charter	3	1	24
PB02	Requirement Analysis	8	1	64
PB03	Stakeholder Identification	2	1	16
PB04	Architecture Design	5	2	80
PB05	Database Design	5	2	80
PB06	UI/UX Prototyping	5	3	120
PB07	Frontend Development	13	3	312
PB08	Backend Development	13	3	312
PB09	Machine Learning	13	3	312
PB10	Unit & Integration Testing	5	2	80
PB11	Performance & Security Testing	5	1	40
PB12	Model Validation	5	3	120
PB13	Server Setup	5	4	192
PB14	Cloud Configuration	5	3	120
PB15	Deployment to Production	3	3	96
PB16	Phishing Database Update	3	1	24
PB17	Ongoing Model Retraining	3	1	24
PB18	Monitoring	2	1	16

ID	Activity	Story Point (Fibonacci)	Resource (persons)	Effort (hours)
PB19	Documentation (Manual, Report, Source Code)	5	2	80
PB20	Final Project Report & Lessons Learned	3	1	24
PB21	Transfer to IT Operations	2	2	32

➤ **Total duration: 107 days**

➤ **Total effort: 2,168 hours**


V. PERT/CPM

1. Project Activity List and Immediate Predecessors

ID	Activity	Duration (Days)	Immediate Predecessors
PB01	Project Charter	3	
PB02	Requirement Analysis	8	PB01
PB03	Stakeholder Identification	2	PB01
PB04	Architecture Design	5	PB02,PB03
PB05	Database Design	5	PB04
PB06	UI/UX Prototyping	5	PB05
PB07	Frontend Development	13	PB06
PB08	Backend Development	13	PB07
PB09	Machine Learning	13	PB08
PB10	Unit & Integration Testing	5	PB09,PB15
PB11	Performance & Security Testing	5	PB10
PB12	Model Validation	5	PB11
PB13	Server Setup	5	PB08

ID	Activity	Duration (Days)	Immediate Predecessors
PB14	Cloud Configuration	5	PB13
PB15	Deployment to Production	3	PB14
PB16	Phishing Database Update	3	PB12
PB17	Ongoing Model Retraining	3	PB16
PB18	Monitoring	2	PB16
PB19	Documentation (Manual, Report, Source Code)	5	PB17,PB18
PB20	Final Project Report & Lessons Learned	3	PB19
PB21	Transfer to IT Operations	2	PB19

2. PERT DIAGRAM

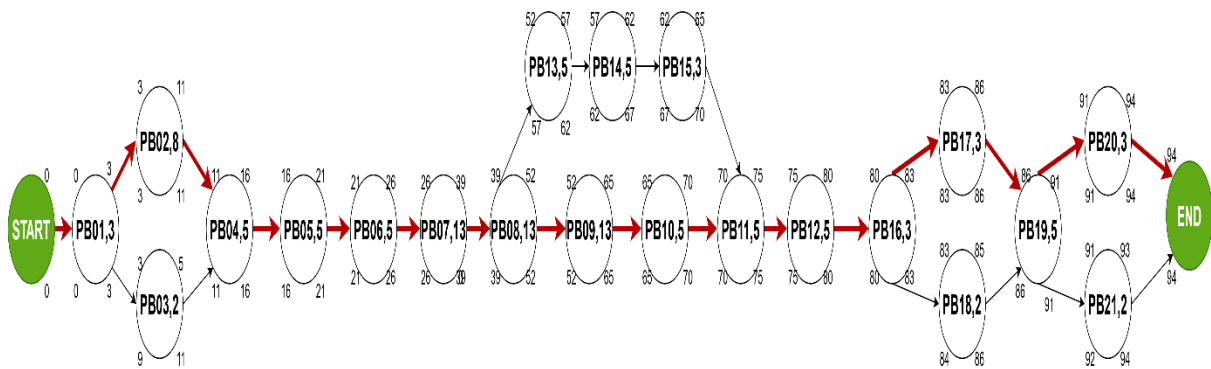

Duration = PB01 → PB02 → PB04 → PB05 → PB06 → PB07 → PB08 → PB09 → PB10 → PB11 → PB12 → PB16 → PB17 → PB19 → PB20 = **94 days**


3. CPM Analysis

ID	ES	EF	LS	LF	Total Slack	Free Slack
PB01	0	3	0	3	0	0
PB02	3	11	3	11	0	0
PB03	3	5	9	11	6	6
PB04	11	16	11	16	0	0
PB05	16	21	16	21	0	0
PB06	21	26	21	26	0	0
PB07	26	39	26	39	0	0
PB08	39	52	39	52	0	0
PB09	52	65	52	65	0	0
PB10	65	70	65	70	0	0
PB11	70	75	70	75	0	0
PB12	75	80	75	80	0	0
PB13	52	57	57	62	5	0
PB14	57	62	62	65	5	0
PB15	62	65	67	70	5	5
PB16	80	83	80	83	0	0
PB17	83	86	83	86	0	0
PB18	83	85	84	86	1	1
PB19	86	91	86	91	0	0
PB20	91	94	91	94	0	0
PB21	91	93	92	94	1	1

Total Slack: PB03(6), PB13(5), PB14(5), PB15(5), PB18(1), PB21(1).

Free Slack: PB03(6), PB15(5), PB18(1), PB21(1)

VI. Gantt Chart

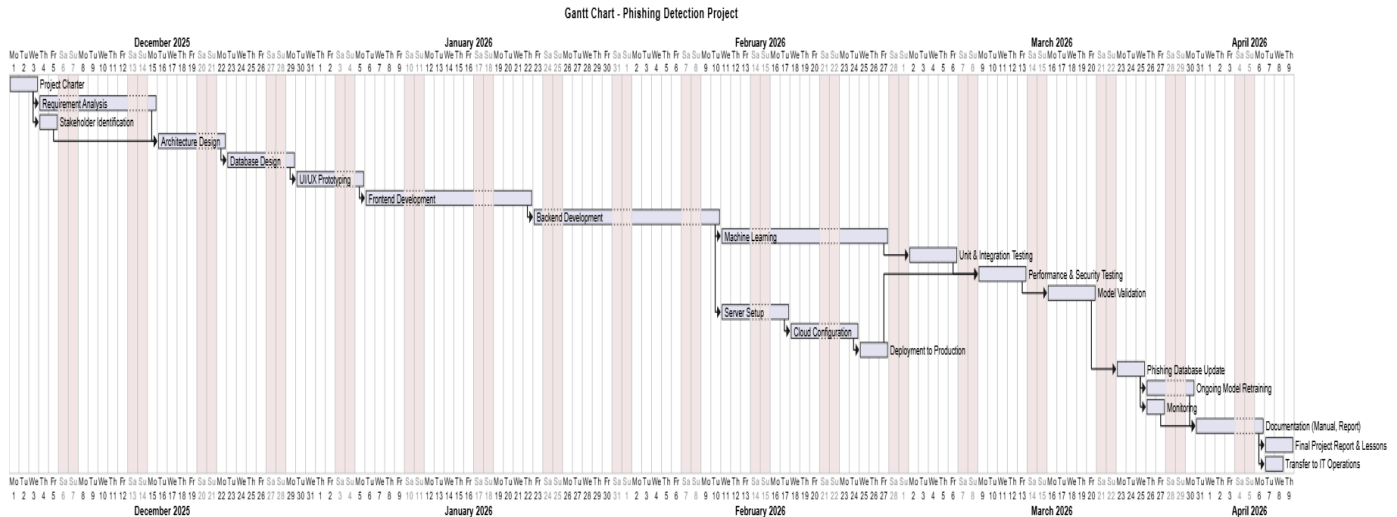

VII. Risk Analysis

ID	Risk Description	Type	P	I	Risk Exposure	Resolution	Explain in detail
1	Poor Input Data Quality: Training data for AI and Blacklist is insufficient or of low quality, leading to false alerts or missed threats.	Technical	3	5	15	- Diversify data sources (OSINT) - Develop automated crawler tools - Apply Feature Engineering and rigorous data cleaning	Proactively using crawler tools and open sources from the start significantly reduces the probability of data shortage compared to manual searching.
2	Sophisticated Phishing Evolution: Attackers employ new techniques that the model has not yet learned, rendering the system obsolete.	Technical	4	4	16	- Implement periodic Retraining pipeline - Combine AI with Blacklist - Allow user error reporting	The system requires a "self-learning" mechanism to keep up with phishing tricks that change daily, rather than relying solely on static data.
3	Budget Shortage: The estimated budget is	Project	3	4	12	- Create detailed budget plan - Utilize Free-	Leveraging student/startup support packages

ID	Risk Description	Type	P	I	Risk Exposure	Resolution	Explain in detail
	insufficient to cover server/AI infrastructure costs as the project expands.					tier/Student pack services - Optimize infrastructure costs	helps reduce initial financial pressure while ensuring stable system operations.
4	Personnel Risk (Fluctuation & Performance): Members are inefficient, delayed, or leave the team abruptly, causing resource shortages and serious knowledge gaps.	Project	3	5	15	- Comprehensive Documentation - Cross-training (Backup) among members - Include Buffer time in planning	Documentation and Cross-training ensure knowledge isn't lost with a single individual. If someone is absent, a backup can use the documentation to take over immediately without disrupting the project.
5	Reputational Damage via Security Breach: The system is exploited (e.g., hackers whitelist malicious sites), leading to complete loss of user trust.	Business/Technical	3	4	12	- Apply "Security by Design" philosophy - Conduct periodic Penetration Testing - Implement Fail-safe mechanisms	For a security product, trust is vital. Proactive offensive testing (Pentest) helps patch vulnerabilities before real hackers can exploit them.
6	Misalignment with User Needs: The interface is difficult to use or features are unrealistic, causing	Business	3	4	12	- Gather early feedback via Beta versions - Optimize for simplest possible UX/UI	End-users are often non-technical, so the product must be extremely simple. Early feedback helps

ID	Risk Description	Type	P	I	Risk Exposure	Resolution	Explain in detail
	general users to reject the product.						avoid wasting effort on unwanted features.
7	Missed Deadline: The workload is too large for the 4-month course duration.	Project	2	5	10	- Adhere to MoSCoW (Prioritize Must-have)	Focus on completing core features (MVP) first to ensure deliverable product; secondary features can be cut if time runs out.

VIII. Budget

1. Human Resources

Role	ID	Activity
1. Project Manager	PB01	Project Charter
	PB03	Stakeholder Identification
	PB20	Final Project Report
2. Business Analyst	PB02	Requirement Analysis
	PB19	Documentation
3. System Architect	PB04	Architecture Design
4. Database Designer	PB05	Database Design
5. UI/UX Designer	PB06	UI/UX Prototyping
6. Frontend Developer	PB07	Frontend Development

Role	ID	Activity
7. Backend Developer	PB08	Backend Development
8. AI Engineer	PB09	Machine Learning
	PB12	Model Validation
	PB17	Ongoing Model Retraining
9. Data Engineer	PB16	Phishing Database Update
10. QA / Tester	PB10	Unit & Integration Testing
	PB11	Performance & Security Testing
11. DevOps Engineer	PB13	Server Setup
	PB14	Cloud Configuration
	PB15	Deployment to Production
	PB18	Monitoring
	PB21	Transfer to IT Operations

- Total Effort: 2,168 hours.
- Human resources budget estimation:

Role	Assigned Tasks	Total Hours (Effort)	Hourly Rate (VND)	Total Amount (VND)
1. Project Manager	PB01, PB03, PB20	64	400,000	25,600,000
2. Business Analyst	PB02, PB19	144	300,000	43,200,000

Role	Assigned Tasks	Total Hours (Effort)	Hourly Rate (VND)	Total Amount (VND)
3. System Architect	PB04	80	500,000	40,000,000
4. Database Designer	PB05	80	450,000	36,000,000
5. UI/UX Designer	PB06	120	250,000	30,000,000
6. Frontend Developer	PB07	312	250,000	78,000,000
7. Backend Developer	PB08	312	250,000	78,000,000
8. AI Engineer	PB09, PB12, PB17	456	350,000	159,600,000
9. Data Engineer	PB16	24	300,000	7,200,000
10. QA / Tester	PB10, PB11	120	180,000	21,600,000
11. DevOps Engineer	PB13, PB14, PB15, PB18, PB21	456	300,000	136,800,000
TOTAL		2,168		656,000,000 VND

2. Reusable Resources

Item	Description	Quantity	Duration	Unit Cost (VND)	Total Cost (VND)
High-Performance Workstations	PC/Laptop for AI & Backend (Depreciation/Rental cost)	3 units	4 months	2,500,000 / month	30,000,000
Standard Workstations	PC/Laptop for Frontend, PM, Tester (Depreciation/Rental cost)	4 units	4 months	1,500,000 / month	24,000,000
Office Workspace	Co-working space rental or Office utility allocation	1 room	4 months	8,000,000 / month	32,000,000
Testing Devices	Mobile devices/Tablets for responsive testing	2 units	4 months	1,000,000 / month	8,000,000
TOTAL REUSABLE					94,000,000 VND

3. Consumed Resources

Item	Description	Quantity	Duration	Unit Cost (VND)	Total Cost (VND)
Cloud Server (GPU)	AWS/GCP Instance for AI Model Training & Inference	1 instance	4 months	5,000,000 / month	20,000,000
Web Hosting & Database	App Server + MySQL Database Hosting	1 package	4 months	2,000,000 / month	8,000,000
Domain Name	Domain registration (.com / .vn)	1 year	1 time	500,000	500,000

Item	Description	Quantity	Duration	Unit Cost (VND)	Total Cost (VND)
Data Acquisition	Purchase of Phishing Datasets / APIs	1 package	1 time	15,000,000	15,000,000
Operational Expenses	Team meals, coffee, electricity, internet	4 months	4 months	6,000,000 / month	24,000,000
Contingency Fund	Risk reserve (Budget Shortage Risk)	10%			15,000,000
TOTAL CONSUMED					82,500,000 VND

4. Total Project Budget Summary

Category	Estimated Cost (VND)	Notes
1. Human Resources	656,000,000	Based on professional hourly rates (PM, AI, Dev, QA).
2. Reusable Resources	94,000,000	Equipment depreciation and workspace rental.
3. Consumed Resources	82,500,000	Cloud infra, data, operations, and contingency.
TOTAL	832,500,000 VND	

5. Financial Feasibility & ROI.

- Initial Investment: 832,500,000 VND.
- Year 1 Estimated Value: 250,000,000 VND.
- Annual Growth Rate: 12%.
- Interest Rate: 10%.

Year	Cash Flow (Estimated Value)	PV (Present Value)	Cumulative Cash Flow	Status
Year 0	-832,500,000	-832,500,000	-832,500,000	Investment Phase
Year 1	250,000,000	227,272,727	-582,500,000	Recovering
Year 2	280,000,000	231,404,959	-302,500,000	Recovering
Year 3	313,600,000	235,612,321	11,100,000	Break-even Point
Year 4	351,232,000	239,896,182	362,332,000	Profit
Year 5	393,379,840	244,257,930	755,711,840	Profit

- Total Revenue (5 Years): 1,588,211,840 VND.
- Net Present Value (NPV): 345,944,120 VND (Positive NPV confirms feasibility).
- Payback Period: ~2.96 Years (Investment recovered by the end of Year 3).
- Return on Investment (ROI): ~91% (over 5 years).

IX. Product Backlog

ID	User Story	Story Point	Priority	Sprint	Estimates Effort
US-A1	As a visitor, I would like to register an account (email + password + optional profile information) so I can use the system to check out sites and save my history.	2	1	1	16
US-A2	As a registered user, I want to log in and out securely so that my personal information and history remain private.	3	1	1	24
US-A3	As a registered user, I want to change my password and reset via email if forgotten so that I can regain access securely.	5	1	1	40
US-B1	As a user, I want to type in a URL and get instant results (safe/suspicious/scam) to know whether to trust that site or not.	3	2	2	24
US-B2	As a user, I would like to see detailed analytics (features used by the classifier: domain age, SSL, domain identity, keywords, etc.) to understand why the site was flagged.	3	2	2	24
US-B3	As a logged in user, I would like to save recent scans to my account so I can review previous checks.	2	2	2	16
US-C1	As an admin, I want to add users that are considered untrustworthy or dangerous to a blacklist so that the system immediately blocks or flags them.	2	3	3	16
US-C2	As an admin, I want to edit or delete blacklist entries so that I can correct false positives.	1	3	3	8
US-C3	As an admin, I want to import/export blacklist data	5	3	3	40

ID	User Story	Story Point	Priority	Sprint	Estimates Effort
	(CSV/MySQL) so we can maintain a large verified database.				
US-D1	As a system, I want a classification model that evaluates URLs using URL features, domain recognition, security, and encryption so that the system can automatically detect suspicious websites.	3	5	5	24
US-D2	As a PO/engineering lead, I want to have reporting on model accuracy on validation/test sets and metrics so we can maintain our target of >90% accuracy.	2	5	5	16
US-D3	As a data engineer, I want to have a pipeline to retrain the model with updated labeled data so that the system can improve its detection ability over time.	5	5	5	40
US-E1	As a user, I want to give feedback (“is this a scam” / “is this safe”) on the scan results so the system can get human input to improve the blacklist/model.	5	4	4	40
US-E2	As an admin, I would like to have a queue of user reported URLs to review so I can validate and update blacklist or model labels.	5	4	4	40
US-F1	As a project, we wanted to have a MySQL database containing ≥ 500 verified and continuously updated phishing sites so that the model and tests use rich and up-to-date data.	2	3	3	16
US-F2	As a system, I want DB queries to check URLs to respond within a target time (ex : ≤ 5 seconds) so that the user has a fast experience.	2	2	2	16
US-G1	As a new user, I want clear instructions and explanations of	2	6	6	16


ID	User Story	Story Point	Priority	Sprint	Estimates Effort
	the tool's functionality so I can trust and know how to use it.				
US-G2	As an admin, I want to be notified when important events occur (ex : model drop, large report volume) so I can respond quickly.	2	6	6	16
US-H1	As a system owner, I want user credentials and sensitive data stored securely (hashed passwords, HTTPS) so user data is protected.	3	6	6	24
US-H2	As a product owner, I want the web application to be able to handle the expected amount of concurrent users without taking more than 5 seconds to respond so that users can check the site quickly.	3	6	6	24

X. Burndown Chart

1. Sprint 1


Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Nguyen Xuan Loc	2	1	2	0	0	0	0	0	0	0	0
Nguyen Xuan Loc	2	0	0	1	1	0	0	0	0	0	0
Nguyen Xuan Loc	4	0	0	0	0	3	1	0	0	0	0
Nguyen Xuan Loc	8	0	0	0	0	0	0	3	2	1	1
Tran Viet Loc	4	2	2	0	0	0	0	0	0	0	0
Tran Viet Loc	6	0	0	3	3	0	0	0	0	0	0

Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Tran Viet Loc	4	0	0	0	0	2	2	0	0	0	0
Tran Viet Loc	10	0	0	0	0	0	0	5	3	1	1
Dang Dai Viet	4	3	1	0	0	0	0	0	0	0	0
Dang Dai Viet	4	0	0	2	2	0	0	0	0	0	0
Dang Dai Viet	8	0	0	4	3	1	0	0	0	0	0
Dang Dai Viet	8	0	0	0	0	0	4	4	0	0	0
Dang Dai Viet	16	0	0	0	0	0	2	2	5	4	3
Remaining effort	80	74	69	59	50	44	35	21	11	5	0
Ideal trend	80	72	64	56	48	40	32	24	16	8	0

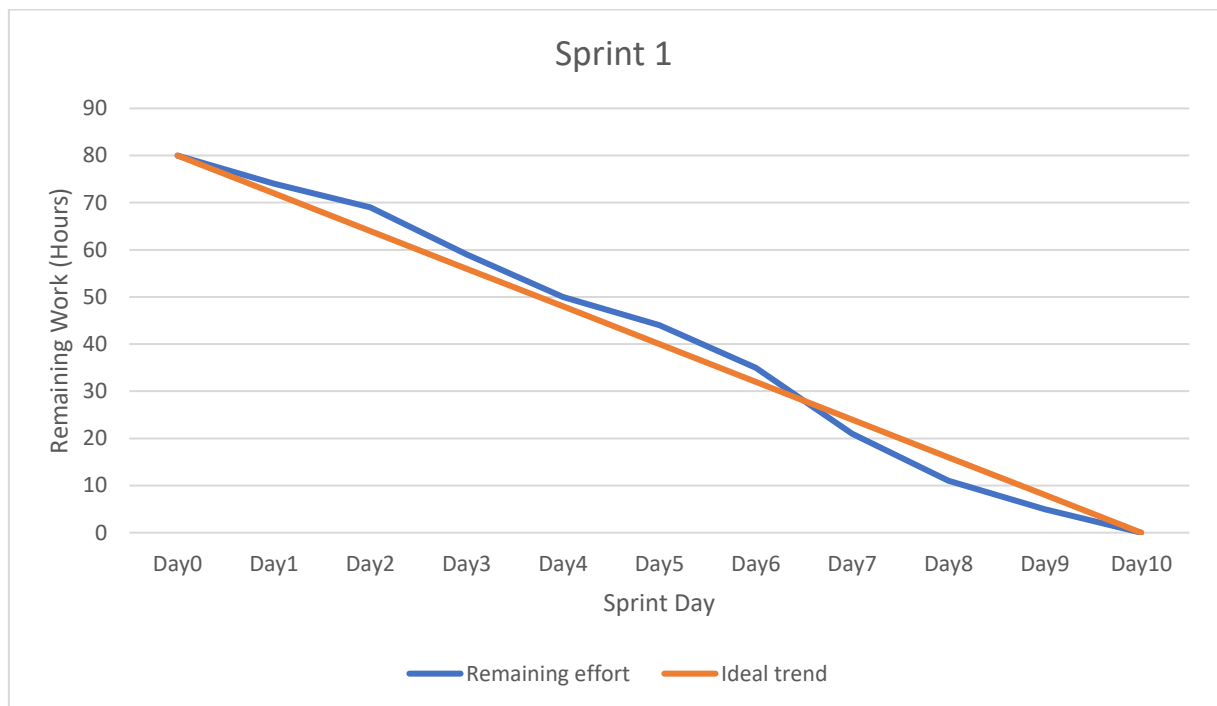

2. Sprint 2


Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Le Minh Truong Kha	4	2	2	0	0	0	0	0	0	0	0
Le Minh Truong Kha	6	0	0	3	3	0	0	0	0	0	0
Le Minh Truong Kha	6	0	0	0	0	3	2	1	0	0	0
Le Minh Truong Kha	8	0	0	0	0	0	0	0	4	3	1
Nguyen Van Duy Manh	7	4	2	1	0	0	0	0	0	0	0
Nguyen Van Duy Manh	7	0	0	0	3	3	1	0	0	0	0
Nguyen Van Duy Manh	10	0	0	0	0	0	0	4	3	2	1
Nguyen Xuan Loc	2	1	2	0	0	0	0	0	0	0	0
Nguyen Xuan Loc	2	0	0	1	1	0	0	0	0	0	0
Nguyen Xuan Loc	4	0	0	0	0	3	1	0	0	0	0
Nguyen Xuan Loc	8	0	0	0	0	0	0	3	2	1	1
Tran Viet Loc	8	2	2	2	1	1	0	0	0	0	0
Tran Viet Loc	8	0	0	0	0	0	2	2	2	1	1
Remainin g effort	80	71	63	56	48	38	32	22	11	4	0
Ideal trend	80	72	64	56	48	40	32	24	16	8	0

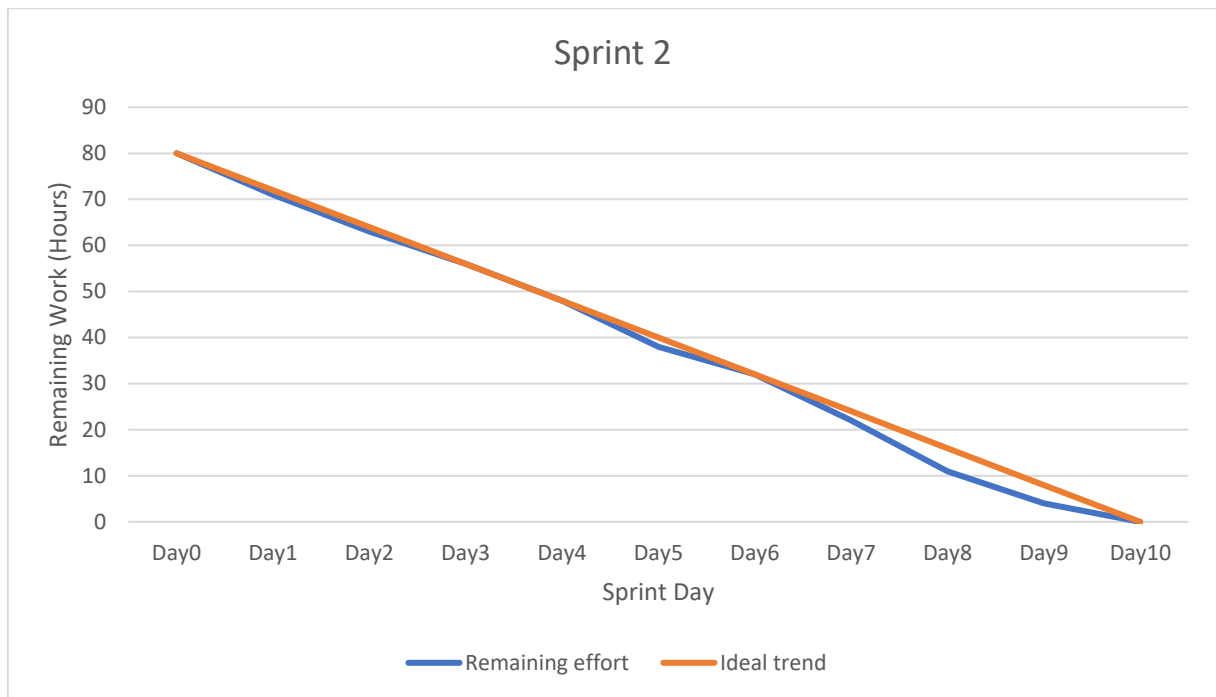

3. Sprint 3


Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Le Minh Truong Kha	2	1	2	0	0	0	0	0	0	0	0
Le Minh Truong Kha	2	0	0	1	1	0	0	0	0	0	0
Le Minh Truong Kha	4	0	0	0	0	3	1	0	0	0	0
Le Minh Truong Kha	8	0	0	0	0	0	0	3	2	1	1
Dang Dai Viet	2	1	1	0	0	0	0	0	0	0	0
Dang Dai Viet	2	0	0	1	1	0	0	0	0	0	0
Dang Dai Viet	2	0	0	0	0	1	1	0	0	0	0
Dang Dai Viet	2	0	0	0	0	0	0	1	1	0	0
Nguyen Xuan Loc	8	4	2	2	0	0	0	0	0	0	0
Nguyen Xuan Loc	12	0	0	0	6	6	0	0	0	0	0

Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Nguyen Xuan Loc	8	0	0	0	0	0	6	2	0	0	0
Nguyen Xuan Loc	12	0	0	0	0	0	0	0	8	2	2
Tran Viet Loc	8	2	2	2	1	1	0	0	0	0	0
Tran Viet Loc	8	0	0	0	0	0	2	2	2	1	1
Remaining effort	80	72	65	59	50	39	29	21	8	4	0
Ideal trend	80	72	64	56	48	40	32	24	16	8	0

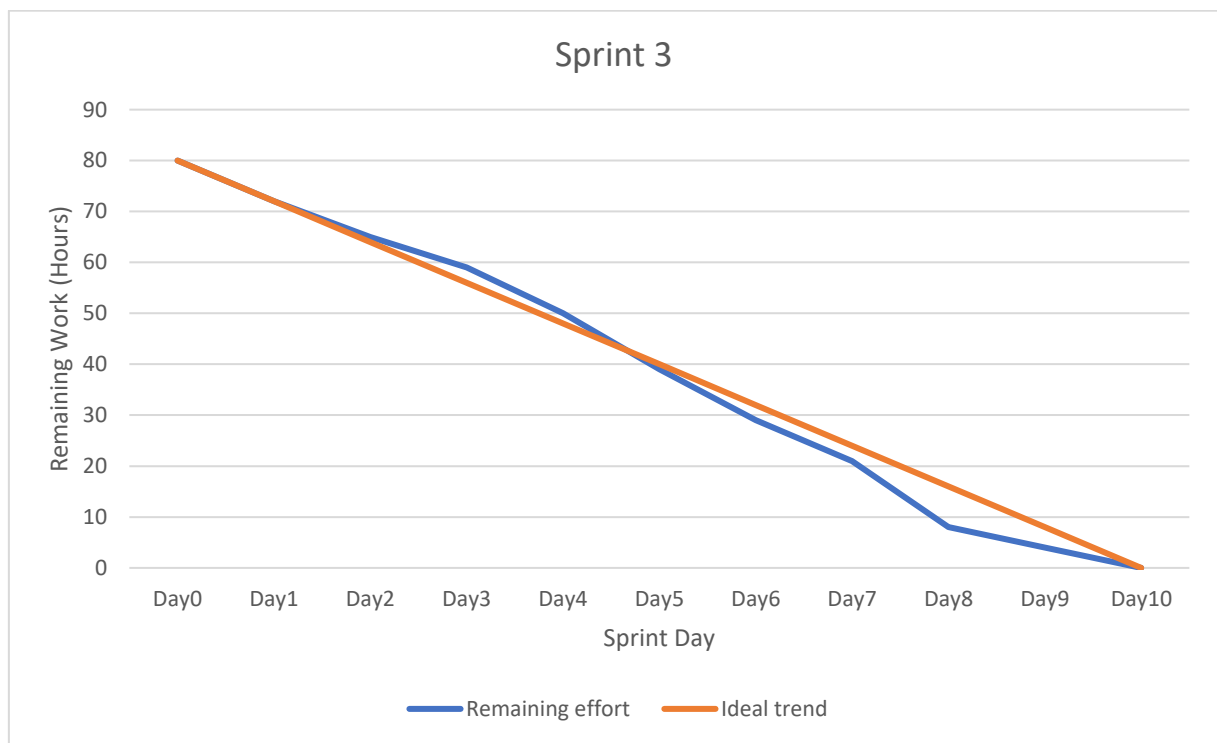

4. Sprint 4


Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Le Minh Truong Kha	8	4	2	2	0	0	0	0	0	0	0
Le Minh Truong Kha	12	0	0	0	6	6	0	0	0	0	0
Le Minh Truong Kha	8	0	0	0	0	0	6	2	0	0	0
Le Minh Truong Kha	12	0	0	0	0	0	0	0	8	2	2
Dang Dai Viet	8	4	2	2	0	0	0	0	0	0	0
Dang Dai Viet	12	0	0	0	6	6	0	0	0	0	0
Dang Dai Viet	8	0	0	0	0	0	6	2	0	0	0
Dang Dai Viet	12	0	0	0	0	0	0	0	8	2	2
Remaining effort	80	72	68	64	52	40	28	24	8	4	0
Ideal trend	80	72	64	56	48	40	32	24	16	8	0

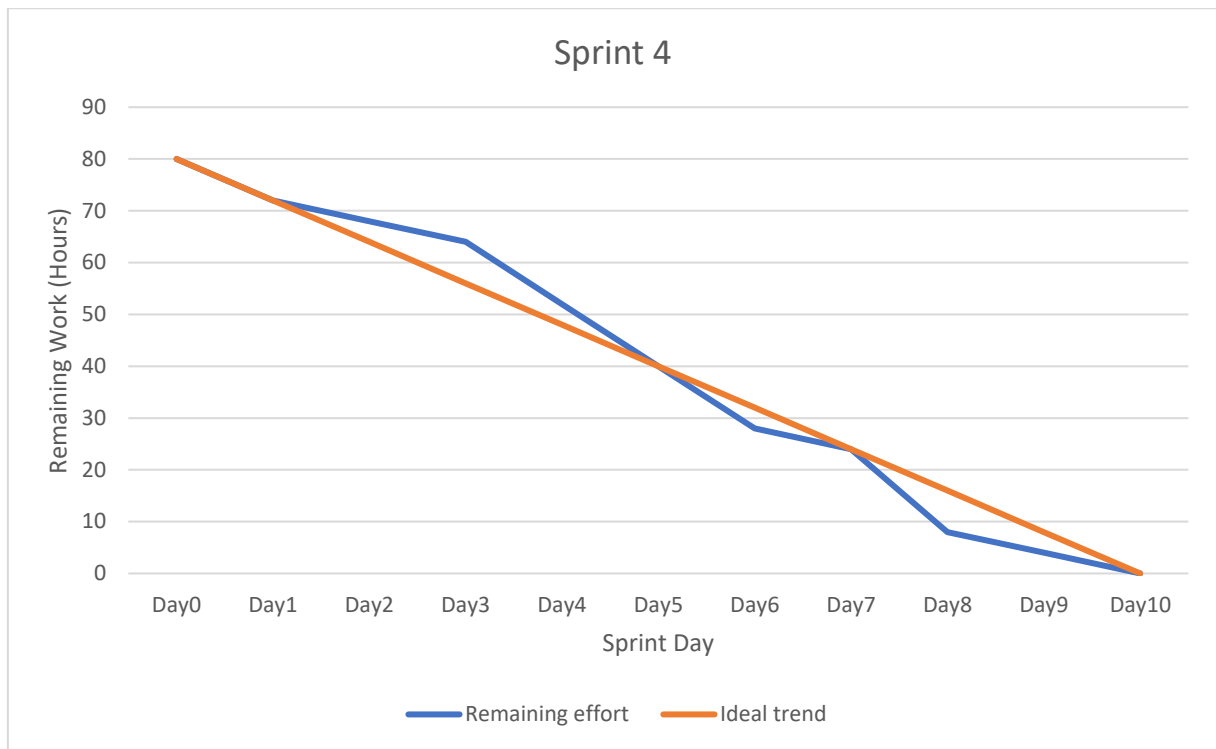

5. Sprint 5

Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Tran Viet Loc	7	4	2	1	0	0	0	0	0	0	0
Tran Viet Loc	7	0	0	0	3	3	1	0	0	0	0
Tran Viet Loc	10	0	0	0	0	0	0	4	3	2	1
Le Minh Truong Kha	4	2	2	1	0	0	0	0	0	0	0
Le Minh Truong Kha	4	0	0	0	2	1	0	0	0	0	0
Le Minh Truong Kha	8	0	0	0	0	0	0	4	2	1	1
Nguyen Van Duy Manh	8	4	2	2	0	0	0	0	0	0	0
Nguyen Van Duy Manh	12	0	0	0	6	6	0	0	0	0	0


Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Nguyen Van Duy Manh	8	0	0	0	0	0	6	2	0	0	0
Nguyen Van Duy Manh	12	0	0	0	0	0	0	0	8	2	2
Remaining effort	80	70	64	60	49	39	32	22	9	4	0
Ideal trend	80	72	64	56	48	40	32	24	16	8	0

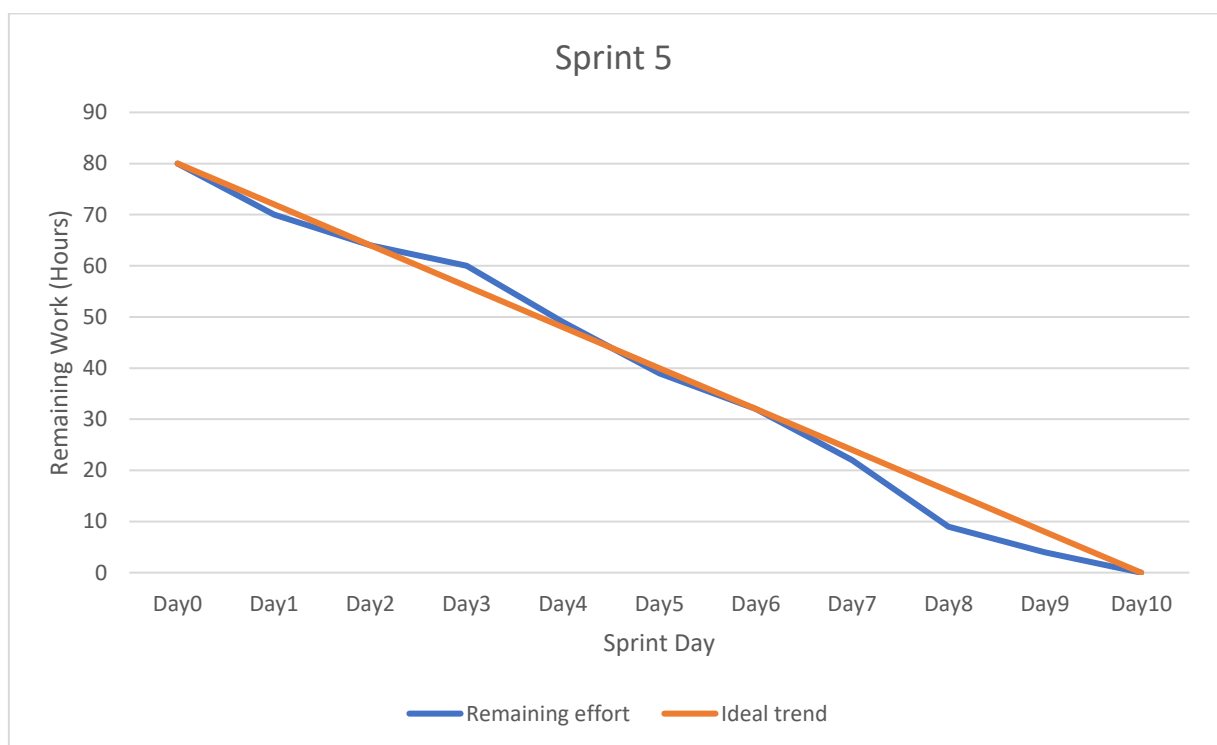

6. Spint 6

Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Tran Viet Loc	8	2	2	2	1	1	0	0	0	0	0
Tran Viet Loc	8	0	0	0	0	0	2	2	2	1	1
Le Minh Truong Kha	4	2	2	1	0	0	0	0	0	0	0

Owner	Day 0	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
Le Minh Truong Kha	4	0	0	0	2	1	0	0	0	0	0
Dang Dai Viet	8	0	0	0	0	0	0	4	2	1	1
Nguyen Xuan Loc	12	4	2	2	2	2	0	0	0	0	0
Nguyen Xuan Loc	12	0	0	0	0	0	4	2	2	2	2
Nguyen Van Duy Manh	12	4	2	2	2	2	0	0	0	0	0
Nguyen Van Duy Manh	12	0	0	0	0	0	4	2	2	2	2
Remaining effort	80	68	60	53	46	40	30	20	12	6	0
Ideal trend	80	72	64	56	48	40	32	24	16	8	0

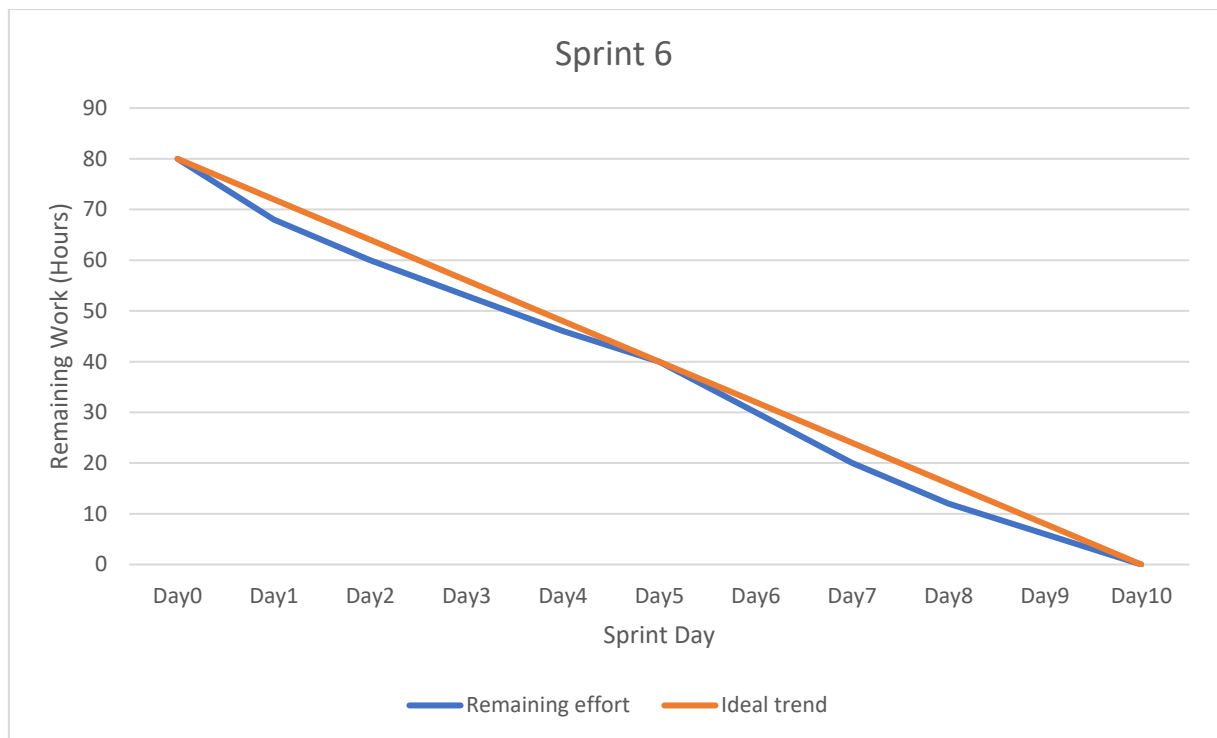

XI. Sprint Backlog

1. Sprint 1

US ID	Task	Owner	Estimates Effort	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
US-A1	Registration UI	Nguyen Xuan Loc	2	1	2	0	0	0	0	0	0	0	0
	Registration API	Nguyen Xuan Loc	2	0	0	1	1	0	0	0	0	0	0
	Email Activation Service	Nguyen Xuan Loc	4	0	0	0	0	3	1	0	0	0	0
	Account Activation Flow	Nguyen Xuan Loc	8	0	0	0	0	0	0	3	2	1	1
US-A2	Login UI	Tran Viet Loc	4	2	2	0	0	0	0	0	0	0	0
	Login API	Tran Viet Loc	6	0	0	3	3	0	0	0	0	0	0
	Logout API	Tran Viet Loc	4	0	0	0	0	2	2	0	0	0	0
	Security Middleware (Brute-force / Rate Limit)	Tran Viet Loc	10	0	0	0	0	0	0	5	3	1	1
US-A3	Change Password UI	Dang Dai Viet	4	3	1	0	0	0	0	0	0	0	0
	Forgot Password UI	Dang Dai Viet	4	0	0	2	2	0	0	0	0	0	0
	Forgot Password API	Dang Dai Viet	8	0	0	4	3	1	0	0	0	0	0
	Reset Password API	Dang Dai Viet	8	0	0	0	0	0	4	4	0	0	0
	Password Policy Enforcement	Dang Dai Viet	16	0	0	0	0	0	2	2	5	4	3
			80	74	69	59	50	44	35	21	11	5	0

2. Sprint 2

US ID	Task	Owner	Estimates Effort	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
US-B1	Scan URL UI	Le Minh Truong Kha	4	2	2	0	0	0	0	0	0	0	0
	Scan URL API	Le Minh Truong Kha	6	0	0	3	3	0	0	0	0	0	0
	Fast-path Cache	Le Minh Truong Kha	6	0	0	0	0	3	2	1	0	0	0
	Scan API Performance Optimization	Le Minh Truong Kha	8	0	0	0	0	0	0	0	4	3	1
US-B2	Scan Detail UI	Nguyen Van Duy Manh	7	4	2	1	0	0	0	0	0	0	0
	Scan Detail API	Nguyen Van Duy Manh	7	0	0	0	3	3	1	0	0	0	0
	Feature Breakdown Mapping	Nguyen Van Duy Manh	10	0	0	0	0	0	0	4	3	2	1
US-B3	Scan History UI	Nguyen Xuan Loc	2	1	2	0	0	0	0	0	0	0	0
	Scan History API	Nguyen Xuan Loc	2	0	0	1	1	0	0	0	0	0	0
	Delete History API	Nguyen Xuan Loc	4	0	0	0	0	3	1	0	0	0	0
	History Access Control Security	Nguyen Xuan Loc	8	0	0	0	0	0	0	3	2	1	1
US-F2	DB Index Optimization	Tran Viet Loc	8	2	2	2	1	1	0	0	0	0	0
	Redis Cache Setup	Tran Viet Loc	8	0	0	0	0	0	2	2	2	1	1
			80	71	63	56	48	38	32	22	11	4	0

3. Sprint 3

US ID	Task	Owner	Estimates Effort	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
US-C1	Blacklist Add UI	Le Minh Truong Kha	2	1	2	0	0	0	0	0	0	0	0
	Blacklist Add API	Le Minh Truong Kha	2	0	0	1	1	0	0	0	0	0	0
	Audit Log	Le Minh Truong Kha	4	0	0	0	0	3	1	0	0	0	0
	Cache Invalidation	Le Minh Truong Kha	8	0	0	0	0	0	0	3	2	1	1
US-C2	Edit/Delete UI	Dang Dai Viet	2	1	1	0	0	0	0	0	0	0	0
	Edit API	Dang Dai Viet	2	0	0	1	1	0	0	0	0	0	0
	Delete API	Dang Dai Viet	2	0	0	0	0	1	1	0	0	0	0
	Change Audit Log	Dang Dai Viet	2	0	0	0	0	0	0	1	1	0	0
US-C3	Import UI	Nguyen Xuan Loc	8	4	2	2	0	0	0	0	0	0	0
	CSV Import Worker	Nguyen Xuan Loc	12	0	0	0	6	6	0	0	0	0	0
	CSV Export API	Nguyen Xuan Loc	8	0	0	0	0	0	6	2	0	0	0
	Validation Error Report Engine	Nguyen Xuan Loc	12	0	0	0	0	0	0	0	8	2	2
US-F1	Initial Blacklist Ingestion Script	Tran Viet Loc	8	2	2	2	1	1	0	0	0	0	0
	DB Schema Finalization	Tran Viet Loc	8	0	0	0	0	0	2	2	2	1	1
			80	72	65	59	50	39	29	21	8	4	0

4. Sprint 4

US ID	Task	Owner	Estimates Effort	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
US-E1	Feedback Widget UI	Le Minh Truong Kha	8	4	2	2	0	0	0	0	0	0	0
	Feedback Submit API	Le Minh Truong Kha	12	0	0	0	6	6	0	0	0	0	0
	Feedback Table	Le Minh Truong Kha	8	0	0	0	0	0	6	2	0	0	0
	Feedback ML Label Queue Producer	Le Minh Truong Kha	12	0	0	0	0	0	0	0	8	2	2
US-E2	Admin Report Queue UI	Dang Dai Viet	8	4	2	2	0	0	0	0	0	0	0
	Report List API	Dang Dai Viet	12	0	0	0	6	6	0	0	0	0	0
	Report Triage API	Dang Dai Viet	8	0	0	0	0	0	6	2	0	0	0
	Triage Audit Log	Dang Dai Viet	12	0	0	0	0	0	0	0	8	2	2
			80	72	68	64	52	40	28	24	8	4	0

5. Sprint 5

US ID	Task	Owner	Estimate s Effort	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
US-D1	Model Inference Service	Tran Viet Loc	7	4	2	1	0	0	0	0	0	0	0
	Model Adapter API	Tran Viet Loc	7	0	0	0	3	3	1	0	0	0	0

	ML Contract Test	Tran Viet Loc	10	0	0	0	0	0	0	4	3	2	1
US-D2	Accuracy Metrics Pipeline	Le Minh Truong Kha	4	2	2	1	0	0	0	0	0	0	0
	Accuracy Dashboard	Le Minh Truong Kha	4	0	0	0	2	1	0	0	0	0	0
	Accuracy Alerting System	Le Minh Truong Kha	8	0	0	0	0	0	0	4	2	1	1
US-D3	Dataset Ingestion Service	Nguyen Van Duy Manh	8	4	2	2	0	0	0	0	0	0	0
	Retraining Pipeline	Nguyen Van Duy Manh	12	0	0	0	6	6	0	0	0	0	0
	Model Deployment Pipeline (Canary/Roll back)	Nguyen Van Duy Manh	8	0	0	0	0	0	6	2	0	0	0
	Dataset Snapshot Storage	Nguyen Van Duy Manh	12	0	0	0	0	0	0	0	8	2	2
			80	70	64	60	49	39	32	22	9	4	0

6. Sprint 6

US ID	Task	Owner	Estimates Effort	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	Day 10
US-G1	Homepage UX Content Design	Tran Viet Loc	8	2	2	2	1	1	0	0	0	0	0
	Homepage Responsive UI	Tran Viet Loc	8	0	0	0	0	0	2	2	2	1	1
US-G2	Admin Notification Service	Le Minh	4	2	2	1	0	0	0	0	0	0	0

		Truong Kha											
	Dashboard Alerts UI	Le Minh Truong Kha	4	0	0	0	2	1	0	0	0	0	0
	Notification Threshold Configuration	Dang Dai Viet	8	0	0	0	0	0	0	4	2	1	1
US-H1	Security Hardening Package	Nguyen Xuan Loc	12	4	2	2	2	2	0	0	0	0	0
	OWASP Protection Middleware	Nguyen Xuan Loc	12	0	0	0	0	0	4	2	2	2	2
US-H2	Autoscaling & Rate-Limit Strategy	Nguyen Van Duy Manh	12	4	2	2	2	2	0	0	0	0	0
	Performance Benchmarking Suite	Nguyen Van Duy Manh	12	0	0	0	0	0	4	2	2	2	2
			80	68	60	53	46	40	30	20	12	6	0

XII. Use Tool Click Up

The screenshot displays the ClickUp workspace for 'DuyManh's Workspace'. The interface is organized into a sidebar on the left and a main workspace area. The sidebar contains sections for Home, Favorites, Spaces (including Team Space, Group3, and Sprint Backlog), Channels (General, Welcome, Add Channel), and Direct Messages (Duy Manh, New message). The main workspace area shows a 'Sprint Backlog' view with a table of tasks. The tasks are categorized into three status groups: COMPLETE, IN PROGRESS, and TO DO. Each task entry includes a Name, Assignee (represented by a circular icon with initials), Start date, Due date, Priority (indicated by a colored flag), and Time estimate (indicated by a clock icon). The task list includes 'Sprint 1' (COMPLETE), 'Sprint 2' (IN PROGRESS), and 'Sprint 3' through 'Sprint 6' (TO DO). The bottom of the image shows a Windows taskbar with various application icons and system information, including the date and time (8:39 CH, 08/12/2025).

rollu | Sprint Backlog | DuyManh's Workspace (List)

File Edit View History Window

DuyManh's Workspace

Home

Unread messages

Favorites

Click ☆ to add favorites to your sidebar.

Spaces

☆ All Tasks - DuyManh's Workspa...

Team Space

Group3

Sprint Backlog 5

Project 1

Project 3

Project Notes

+ New Space

Channels

General - DuyManh's Workspace

Welcome

+ Add Channel

Direct Messages

Duy Manh — You

+ New message

Customize Sidebar

Team Space / Group3 / Sprint Backlog

Add Channel rollu Board Calendar Gantt Table + View

Group: Status Subtasks Columns

Save view Filter Closed Assignee Customize Add Task

COMPLETE 1 ... +

Name	Assignee	Start date	Due date	Priority	Time estimate
Sprint 1 3	DM LX	12/1/25	Sun	Urgent	80h
Registration UI	LX	12/1/25	6 days ago	Urgent	2h
Registration API	LX	5 days ago	4 days ago	Urgent	2h
Email Activation Service	LX	3 days ago	Today	Urgent	4h
Account Activation Flow	LX	Tomorrow	Wed	Urgent	8h
US-A2 4	T	12/1/25	Fri	Urgent	24h
Login UI	T	12/1/25	6 days ago	Urgent	4h
Login API	T	5 days ago	4 days ago	Urgent	6h
Logout API	T	3 days ago	Today	Urgent	4h
Security Middleware	T	Tomorrow	Fri	Urgent	10h
US-A3 5	DM	12/1/25	Fri	Urgent	40h
Change Password UI	DM	12/1/25	6 days ago	Urgent	4h
Forgot Password UI	DM	5 days ago	4 days ago	Urgent	4h
Forgot Password API	DM	5 days ago	4 days ago	Urgent	8h
Reset Password API	DM	3 days ago	Today	Urgent	8h

22°C Có mây

Search

VIE 8:40 CH 08/12/2025

rollu | Sprint Backlog | DuyManh's Workspace (List)

File Edit View History Window

DuyManh's Workspace

Home

Unread messages

Favorites

Click ☆ to add favorites to your sidebar.

Spaces

☆ All Tasks - DuyManh's Workspa...

Team Space

Group3

Sprint Backlog 5

Project 1

Project 3

Project Notes

+ New Space

Channels

General - DuyManh's Workspace

Welcome

+ Add Channel

Direct Messages

Duy Manh — You

+ New message

Customize Sidebar

Team Space / Group3 / Sprint Backlog

Add Channel rollu Board Calendar Gantt Table + View

Group: Status Subtasks Columns

Save view Filter Closed Assignee Customize Add Task



IN PROGRESS 1 ... +

Name	Assignee	Start date	Due date	Priority	Time estimate
Sprint 2 4	DM TL LX	12/15/25	12/28/25	High	80h
US-B1 4	TL	12/15/25	12/26/25	High	24h
Scan URL UI	TL	12/15/25	12/16/25	High	4h
Scan URL API	TL	12/17/25	12/18/25	High	6h
Fast-path Cache	TL	12/19/25	12/23/25	High	6h
Scan API Performance Optimization	TL	12/24/25	12/26/25	High	8h
US-B2 3	DM	12/15/25	12/26/25	High	24h
Scan Detail UI	DM	12/15/25	12/17/25	High	7h
Scan Detail API	DM	12/18/25	12/22/25	High	7h
Feature Breakdown Mapping	DM	12/23/25	12/26/25	High	10h
US-B3 4	LX	12/15/25	12/27/25	High	16h
Scan History UI	LX	12/15/25	12/17/25	High	2h
Scan History API	LX	12/18/25	12/19/25	High	2h
Delete History API	LX	12/22/25	12/23/25	High	4h


22°C Có mây

Search

VIE 8:42 CH 08/12/2025

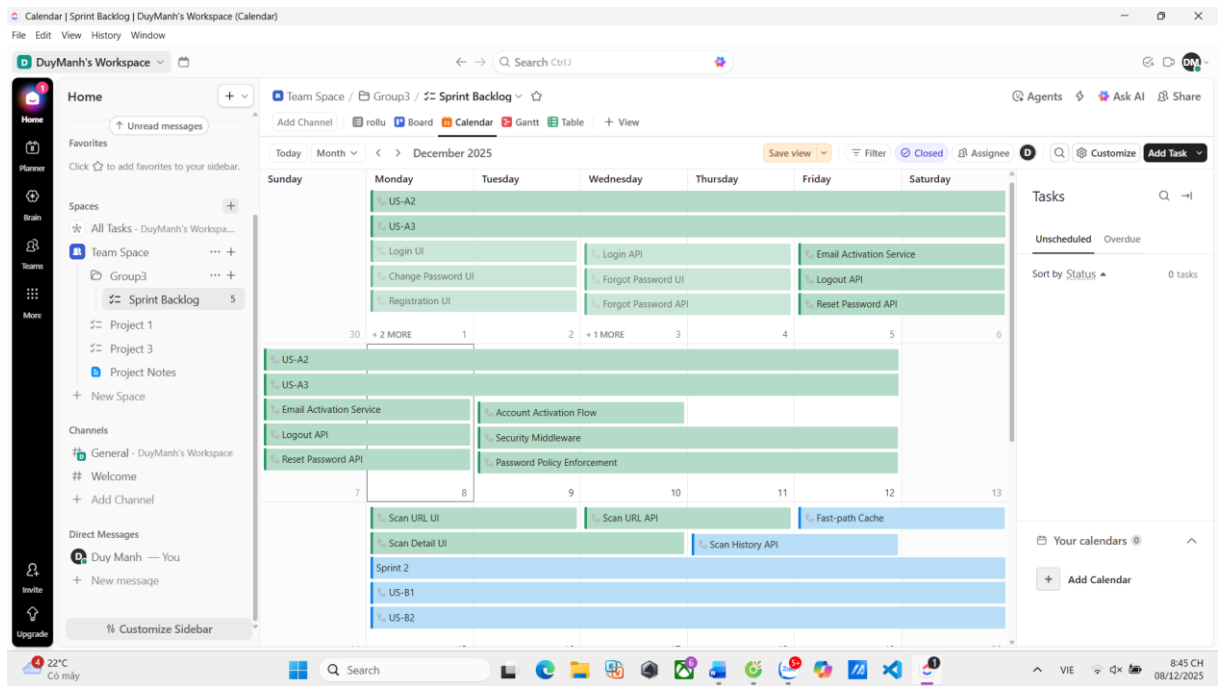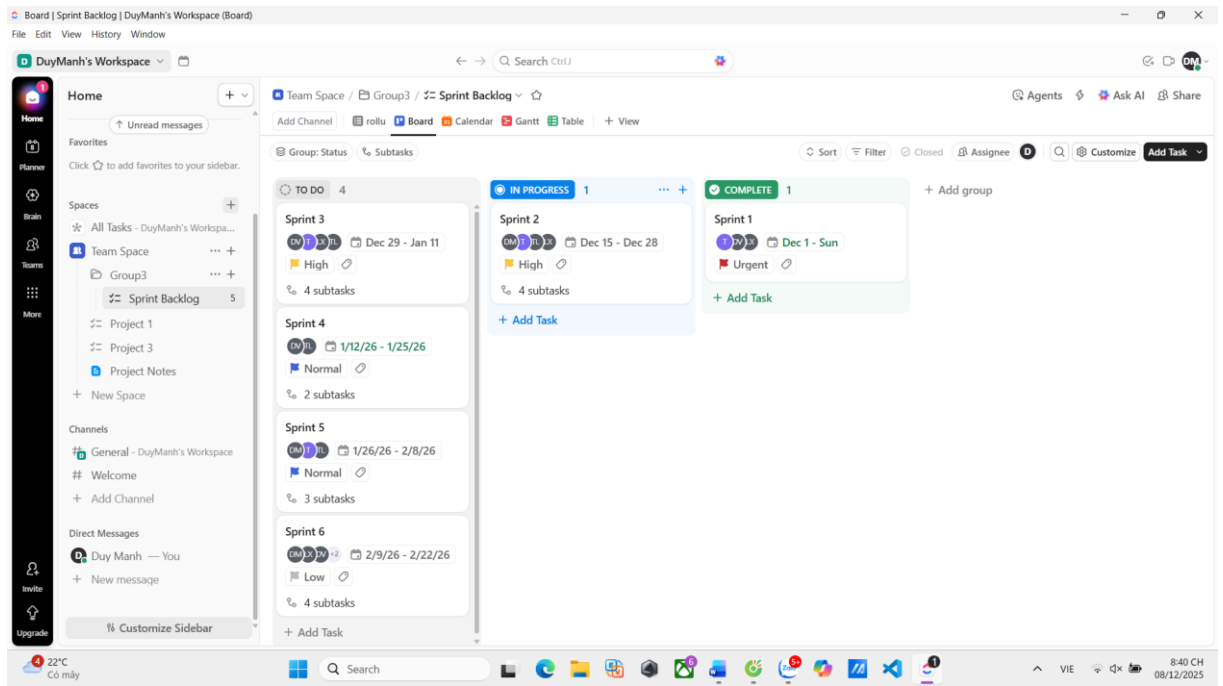

XIII. Demo Interface

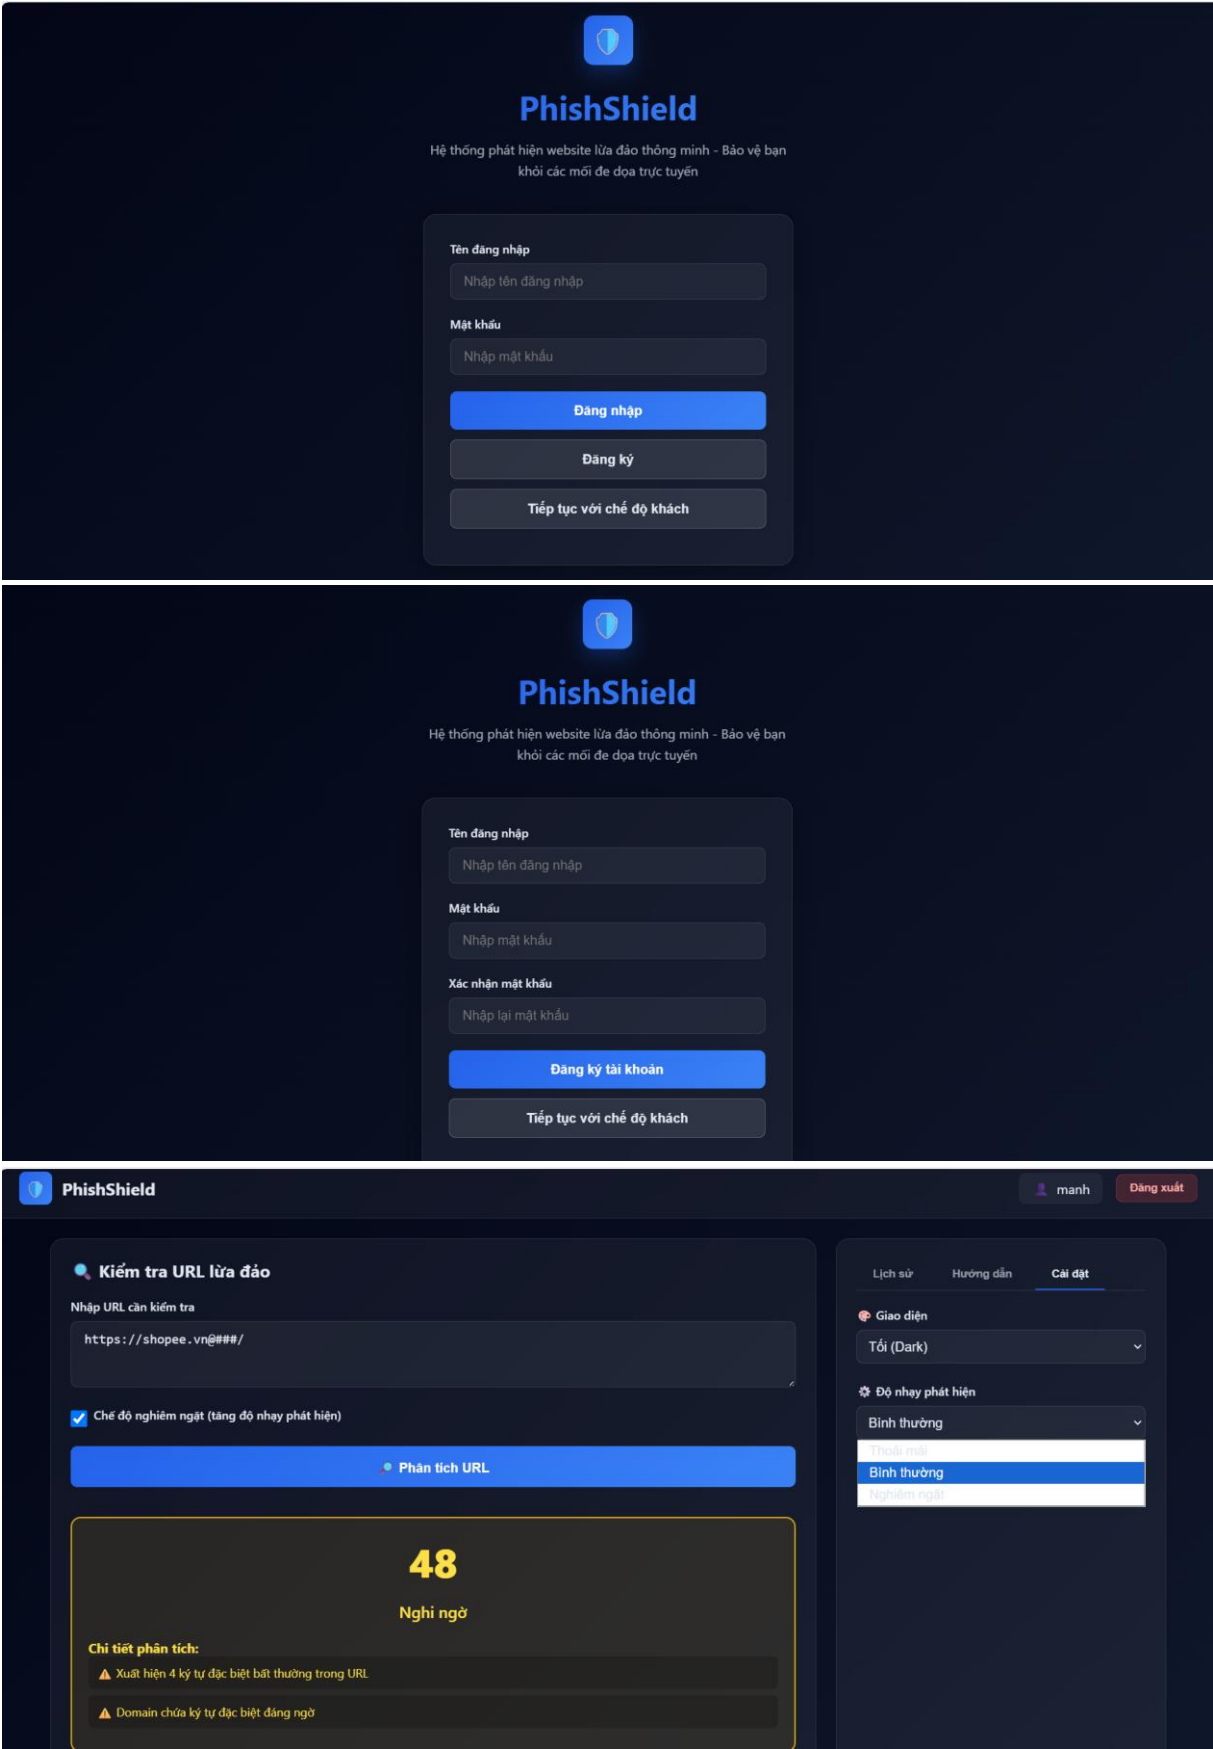

PhishShield

manhĐăng xuất

Kiểm tra URL lừa đảo

Nhập URL cần kiểm tra

https://www.youtube.com/

☒ Chế độ nghiêm ngặt (tăng độ nhạy phát hiện)

Phân tích URL

0

Có vẻ an toàn

Chi tiết phân tích:

Không phát hiện dấu hiệu đáng ngờ rõ ràng

Lịch sửHướng dẫnCài đặt

Các mức độ rủi ro

An toàn (0-30): URL có vẻ đáng tin cậy, ít dấu hiệu nghi ngờ.

Nghi ngờ (31-70): URL có một số dấu hiệu đáng lo ngại, cần thận trọng.

Rất nguy hiểm (71-100): URL có nhiều dấu hiệu lừa đảo, không nên truy cập.

Lưu ý quan trọng

Hệ thống này chỉ mang tính chất tham khảo, dựa trên các quy tắc phát hiện cơ bản. Không thay thế các giải pháp bảo mật chuyên nghiệp.

Luôn cảnh giác với các URL lạ, đặc biệt là những URL yêu cầu thông tin cá nhân, mật khẩu, hoặc thông tin tài chính.

PhishShield

manhĐăng xuất

Kiểm tra URL lừa đảo

Nhập URL cần kiểm tra

1865Plus_U_SHP-CrossBorder_NotNUI_MultiCrossBorderFrame&utm_id=120236491232730435&fbclid=IwY2xjawOjtzJleHRuA2F1bQIxMABicm1kETFDdVhwQ1dsVHU8NM41ZTdUc3J0YwZhcHBfawQmIyMDM5MTc4ODIwMDg5MgABHv1VlnKIF6GH1GeTnyjmf9AQuNDCsP4OR2RKfmr7rCPjDgTeB_gkt60PSgm0_aem_dZ5KxDoI4MHBG5NmPKTw_g

☒ Chế độ nghiêm ngặt (tăng độ nhạy phát hiện)

Phân tích URL

59

Nghi ngờ

Chi tiết phân tích:

URL quá dài (526 ký tự) - có thể đang cố che giấu nội dung đáng ngờ

Xuất hiện 18 ký tự đặc biệt bất thường trong URL

Lịch sửHướng dẫnCài đặt

https://shopee.vn/lp/meta/78880233/2...
Nghi ngờ (59)20:52:34 8/12/2025

https://shopee.vn/lp/meta/78880233/2...
Rất nguy hiểm (88)20:52:32 8/12/2025

https://shopee.vn/lp/meta/78880233/2...
Nghi ngờ (59)20:52:28 8/12/2025

https://shopee.vn/lp/meta/78880233/2...
Nghi ngờ (41)20:51:46 8/12/2025

https://www.youtubeeeee.com/
Rất nguy hiểm (100)20:50:53 8/12/2025

https://www.youtube.com/

PhishShield

manhĐăng xuất

Kiểm tra URL lừa đảo

Nhập URL cần kiểm tra

https://www.youtubeeeee.com/

☒ Chế độ nghiêm ngặt (tăng độ nhạy phát hiện)

Phân tích URL

100

Rất nguy hiểm

Chi tiết phân tích:

URL chứa chuỗi ký tự lặp lại bất thường (eeeeee)

URL ở dạng https:// - rất đáng ngờ (giáo thức sai chuẩn)

Lịch sửHướng dẫnCài đặt


https://www.youtubeeeee.com/
Rất nguy hiểm (100)20:50:53 8/12/2025

https://www.youtube.com/
Có vẻ an toàn (0)20:49:55 8/12/2025

https://www.youtube.com/
Có vẻ an toàn (0)20:49:50 8/12/2025

46

XIV. Contribute Work

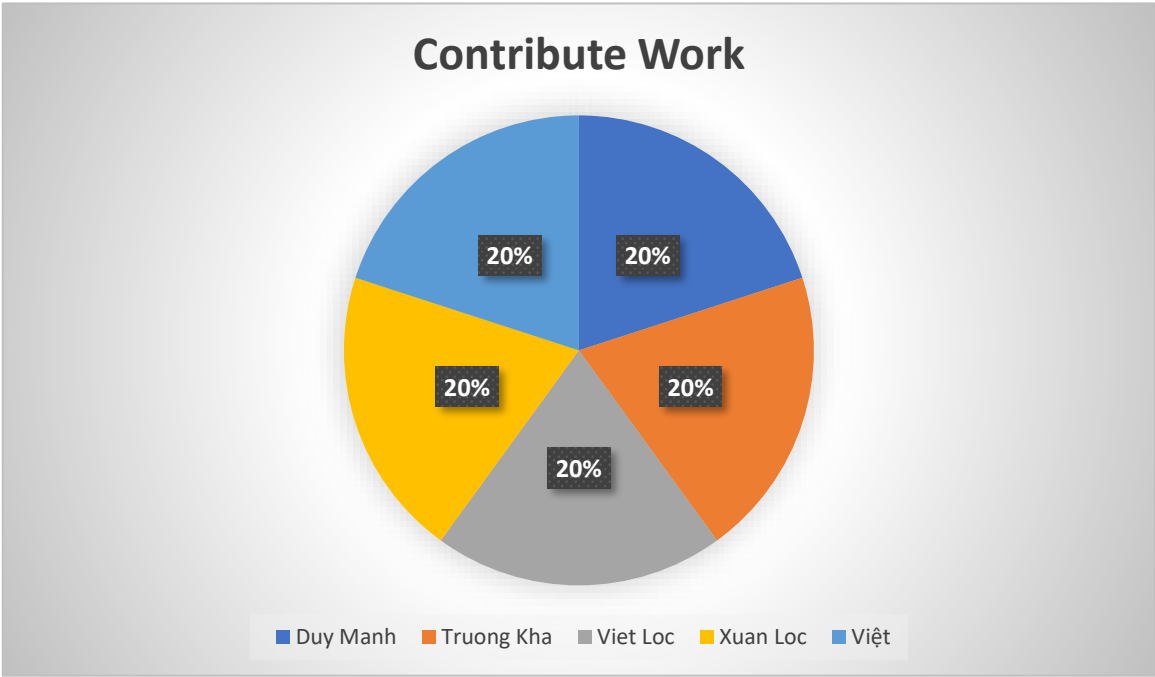

- END -
